UPPER PILUWA KHOLA -3 HYDROELECTRIC PROJECT (4.95 MW)

Sankhuwasabha, Nepal

Progress Report

Date: 12th Baisakh, 2080



Submitted by:



Mabilung Energy Limited. Lalitpur-10, Nepal

Table of Contents

SA	SALIENT FEATURES4				
1	GENERAL	8			
2	PROJECT OVERVIEW	8			
3	CONSTRUCTION WORKS	10			
	3.1 CIVIL WORKS 3.1.1 HEAD WORKS 3.1.2 GRAVEL TRAP, DESANDER AND FORE BAY 3.1.3 WATERWAY ALIGNMENT 3.1.4 POWER HOUSE (PH, SWITCHYARD AND TAIL RACE)	10 10			
	3.2 HYDRO MECHANICAL WORKS	10			
	3.3 ELECTROMECHANICAL WORKS	10			
	3.4 TRANSMISSION LINE	11			
	3.5 RECEIVING END SUBSTATION	11			
4	PHOTOGRAPHS	12			

List of Figures

Figure 4.1: Headworks after final lift concrete	. 12
Figure 4.2: Intake sluice and undersluice structure	. 12
Figure 4.3: Intake sluice and intake structure.	. 13
Figure 4.4: Second stage river diversion	. 13
Figure 4.5: Upstream protection	. 14
Figure 4.6: Downstream protection wall, boulder rip-rap	. 14
Figure 4.7: Rebar installation at Middle cut of weir.	. 15
Figure 4.8: Excavation for upstream cutoff	. 15
Figure 4.9: Settling basin overall structure	. 16
Figure 4.10: Bar laying at settling basing head pond section	. 16
Figure 4.11: Trench excavation for pipe installation.	. 17
Figure 4.12: Headrace pipe installation.	. 17
Figure 4.13: Pipe laying at headrace alignment	. 18
Figure 4.14: Pipe laying with stiffener at headrace alignment	. 18
Figure 4.15 : Pipe laying with upstream protection work	. 19
Figure 4.16 : Anchor block construction at bends	. 19
Figure 4.17: Fabrication of sand flushing chhanel	. 20
Figure 4.18 : Excavation for powerhouse protection work	. 20
Figure 4.19: Excavation and earthmat laying at baneshwor substation work	. 21
Figure 4.19 : Site Visit by Technical consultant along with site technical team	. 21

Mabilung Energy Limited

SALIENT FEATURES

1. Project Details

Project Name : Upper Piluwa Khola 3 Hydroelectric Project

Location : Madi & Chainpur Municipalities,

Sankhuwasabha

Geographical Coordinates : Latitude: 27° 17' 42"N and 27° 18' 04"N

Longitude: 87° 24' 22"E and 87° 25' 30"E

Type of Scheme : Run off River

Installed Capacity : 4.95 MW

Gross Head : 128 m

Rated Design Head : 116.7 m

2. Hydrology

Catchment Area : 83.70 km²

Mean Annual Precipitation : 1500 mm

100 years Design Flood (HW) : 259 m³/s

Design Discharge - Piluwa Khola : 4.11 m³/s

- Sikhuwa Khola : 0.91 m³/s

Mean Annual Discharge- Piluwa Khola: 6.0 m³/s

- Sikhuwa Khola : 1.34 m³/s

Riparian Release - Piluwa Khola : 96 lps

- Sikhuwa Khola : 21 lps

3. Headworks

Diversion Structure : Concrete overflow weir with undersluice

Length of Weir : 25.0 m

Weir crest Elevation : EL 1162 masl

Height of Weir : 7.0 m from bed level at weir

Undersluice : 3 m x 1.75 m - 2 nos

Sill Level : 1157 masl
Intake Type : Side Intake

Size of Opening (B x H) : 3.0 m x 1.2 m - 2 nos

Sill Level : 1160.40 masl

4. Gravel Trap

Type : Rectangular RCC

Particle Size to be settled : 5 mm

Size of Gravel Trap : 8.0 m x 3.3 m (L x B)

5. Approach Canal

Type : RCC Rectangular

Size : 2.2 m x 2.2 m (B x H)

6. Desander

Type : Dufour, double bay

Particle Size to be settled : 0.20 mm

Size of Desander : Each bay of 45 m x 6.4 m (L x B)

7. Sikhuwa Diversion Scheme

Type : Concrete overflow weir

Intake : Side intake of 1.5 m x 0.7 m, 2 nos

Gravel Trap : 2 m deep, 5.0 m long and 1.5 m wide

Transfer Pipe : 0.9 m diameter MS Pipe, 170 m long

8. Headrace Pipe

Total Length : 1398 m

Type : MS-Pipe Buried and exposed section

Diameter of Pipe : 1.366-1.566 m dia with thickness 8 mm

9. Surge tank

Type : Restricted orifice

Size : 4 m diameter 25 m height

10. Penstock Pipe

Total Length : 395 m

Type : MS-Pipe Buried and exposed section

Mabilung Energy Limited

Diameter of Pipe : 1.120 to 1.378 m dia with varied thickness 8

mm to 14 mm

11. Powerhouse

Type : Surface

Dimension (l x b x h) : 23 m x 8.5 m X 11.40 m

PH Floor Level : EL. 1033.10 m

Turbine centerline Level : EL. 1033.50 m

12. Tailrace

Type : 2.0 m wide, 1.6 m high and 25.0 m long, RCC

Box canal

Tailrace Water Level : EL 1034.0 m

Minimum Tail water level : EL 1033.57 m

13. Turbine

Type : 2 Nos. Horizontal Francis

Rated Discharge for each Turbine : 2.51 m³/s

Rated Output for each Unit : 2.578 MW

Rated Efficiency : 90%

14. Generators

Type : 2 Nos. Synchronous brushless, 3Ø AC

Rated Voltage : 6.6 kV

Power Factor : 0.85

Layout : Horizontal

Synchronous speed : 1000 rpm

Rated Efficiency : 96.0 %

Rated Output : 2910 kVA

Rated Frequency : 50 Hz

15. Power Transformer

Type : 1 No. 3 phase, 50 Hz Step up Transformer

Rated Efficiency : 99%

Rate Capacity : 6500 kVA

Voltage Ratio : 33kV/6.6kV

16. Transmission & Interconnection

Transmission line : Powerhouse Baneshwor substation, 14.0 km

Type of Circuit : Single Circuit 33 kV

Line Conductor : ACSR "dog"

Pole Type : Steel Tubular (11 and 13 m height)

17. Power and Energy

Installed Capacity : 4.95 MW

Contract Energy after Outage & Loss : 28.41 GWh

Wet Saleable Energy : 23.51 GWh

Dry Saleable Energy : 4.90 GWh

18. Construction Period : 2.0 Years

19. Financial Indicators

Total Project Cost : 893.37 MNRs. (With IDC)

B/C : 1.27

IRR : 15.23 %

RoE : 18.16 %

1 GENERAL

The progress report has been prepared for updating about the construction and administrative progress of the Upper Piluwa Khola 3 Hydroelectric Project (UPK3HEP).

This report includes the tasks completed until the month of Poush, 2079. This report mainly focuses on the head office status, site office, site visit, design & construction of Project components.

2 PROJECT OVERVIEW

Upper Piluwa Khola-3 Hydroelectric Project is located along the Piluwa Khola between confluence area with Sikhuwa Khola and confluence area with Lakhuwa Khola. The project area lies in Madi and Chainpur Municipalities of Sankhuwasabha District, Province 1 in eastern Nepal, while waterway and powerhouse lies only on Madi Municipality. Chainpur is nearest market place from the project area. Project area is accessible by about 13 km road from Chainpur with a fair weather road. Present updated geographical boundary of project lies between latitude of 27° 17' 42"N and 27° 18' 04"N and longitude of 87° 24' 22"E and 87° 25' 30"E. The elevation at the proposed intake site is 1162 masl. The Project, optimized at an installed capacity of 4.95 MW, is a run-of-the-river type project with gross head of 128 m and design discharge of 5.02 m3/s. Net annual marketable energy to be generated from the Project is 28.41 GWh, out of which 4 .90 GWh is dry season energy (Poush to Baiskah).

The Piluwa Khola is a tributary of Arun River. The basin lies in the eastern part of the Sankhuwasabha district. Elevation of the catchment ranges from 1160 m to 3525 m. The main stream flows from East to West direction. Catchment area at the intake site covers 83.70 km2 out of which 15.18 km2 is covered by Sikhuwa catchment and catchment at powerhouse is 98.50 km2. Design flood at the proposed headworks is taken 259 m3/s (Q100-year). The riparian release for environmental requirement is considered as 0.096 m3/s for Piluwa Khola and 0.021 m3/s for Sikhuwa Khola, which corresponds to 10% of the driest month's flow of the river.

Geologically, the project area lies in Himal Group of Higher Himalayan Crystalline. Present study only covers the rock type and structures found within project area. Bedrocks are partially

exposed at steep slopes and cut bank and road cut sections. Most of the surface within project area is covered with soils.

A diversion weir on Sikhuwa diverts discharge of 0.91 m3/s from Sikhuwa Khola to approach canal from Piluwa Khola diversion works. A spilling weir at Piluwa Khola with two under sluices and two side intake openings will divert the design discharge of 5.02 m3/s to intake structure located at left bank of the river. The diversion structure is design for flood discharge of 259 m3/s. Headworks structure including side intake, gravel trap, approach canal and desander with fore bay are located on left bank of Piluwa Khola. The Headrace pipe from forebay to surge tank is aligned along left bank of Piluwa Khola. After 1360 m length of headrace pipe surge tank is located at left bank hillslope. After surge tank penstock pipe is proposed to be aligned on left bank of Piluwa Khola and the penstock line is designed to cross Lakhuwa Khola to reach Powerhouse. Powerhouse is located at left bank of Piluwa Khola near the confluence Piluwa Khola with Lakhuwa Khola. Powerhouse is dimensioned to accommodate two Francis turbine of horizontal configuration. The switchyard is located just upstream of powerhouse on left bank of Piluwa Khola. About 14 km long 33 kV transmission line connected to Baneshwar substation evacuated the Power generated from UP3HP.

The construction period of the Project has been taken to be 24 months. The total financial cost of the Project on the basis of rates as of January 2020 is estimated to be 893.37 MNRs. with IDC. The Project shall be financed from debt and equity ratio of 70:30 from financing institutions. Financial analysis has been undertaken with 11.75% interest rate on the long-term loan yielding 15.23% IRR, 18.16% RoE, and B/C ratio of 1.27.

3 CONSTRUCTION WORKS

3.1 Civil Works

3.1.1 Head works

- i. Construction of undersluice is completed.
- ii. Construction of upstream protection wall (masonry wall) is completed.
- iii. Construction of intake is completed.
- iv. Construction of approach canal is completed.
- v. Second stage river diversion is accomplished.
- vi. A panel of weir side three cutoffs is completed.
- vii. Excavation and rebar installation for central cutoff is completed.

3.1.2 Gravel trap, Desander and fore bay

- Concreting on all three main panel base slab, inlet transition gate slab of desander is completed.
- ii. Construction of desander shear wall is at final stage of completion.
- iii. Base preparation of downstream forebay accomplished.
- iv. Formworks for shear wall is on progress.

3.1.3 Waterway Alignment

- i. Project road from headworks to surge tank completed.
- ii. Total 700m of trench excavation for laying pipe and bends is completed.
- iii. Excavation for syphon at Sikhuwa crossing is in final stage.
- iv. Track opening from powerhouse to base of gadidanda (0+1700 to 2+000m chainage) is completed.
- v. Total 200 m backfilling at installed pipe trench is completed.

3.1.4 Power House (PH, Switchyard and Tail race)

- i. Excavation of power is completed.
- ii. Excavation for protection wall is on progress.

3.2 Hydro mechanical works

- i. Total 400m headrace pipe and 1bends at headrace alignment is installed.
- ii. Installation of undersluice gate frame is completed.

3.3 Electromechanical Works

- i. Generator is arrived at Nepal boarder and stored at warehouse in Biratnagar.
- ii. Earthing materials, drainage pipes and diesel generator is transported to site.

- iii. EOT crane supplied to site.
- iv. Fabrication of transformer and turbines is completed.

3.4 Transmission Line

- i. Layout drawing of receiving substation is finalized.
- ii. First lot of transmission poles are delivered to site.
- iii. Contractor is mobilized to install transmission pole and accessories.
- iv. Land acquisition for transmission pole erection is completed.

3.5 Receiving end substation

- i. Excavation of receiving substation is completed.
- ii. Laying of earthmat is completed.

4 PHOTOGRAPHS



Figure 4.1: Headworks after final lift concrete.



Figure 4.2: Intake sluice and undersluice structure.



Figure 4.3: Intake sluice and intake structure.



Figure 4.4: Second stage river diversion.



Figure 4.5: Upstream protection.



Figure 4.6: Downstream protection wall, boulder rip-rap.



Figure 4.7: Rebar installation at Middle cut of weir.



Figure 4.8: Excavation for upstream cutoff.



Figure 4.9: Settling basin overall structure.



Figure 4.10: Bar laying at settling basing head pond section..



Figure 4.11: Trench excavation for pipe installation.



Figure 4.12: Headrace pipe installation.



Figure 4.13: Pipe laying at headrace alignment.



Figure 4.14: Pipe laying with stiffener at headrace alignment.



Figure 4.15: Pipe laying with upstream protection work.



Figure 4.16 : Anchor block construction at bends.

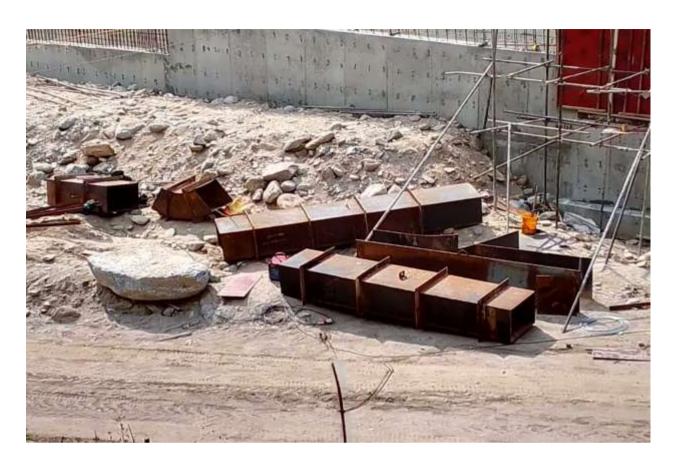


Figure 4.17: Fabrication of sand flushing chhanel.



Figure 4.18: Excavation for powerhouse protection work.

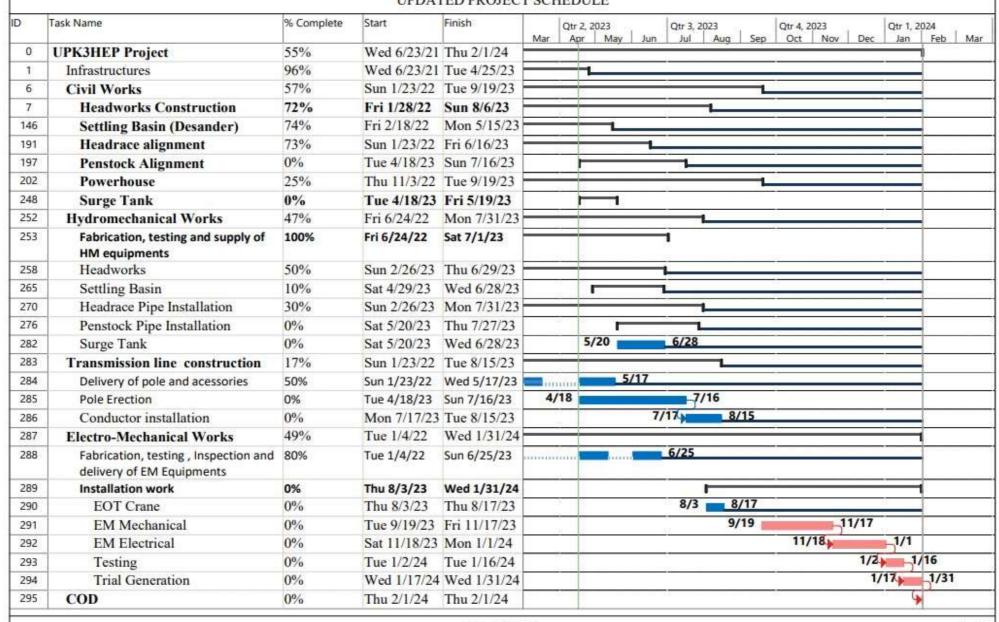


Figure 4.19: Excavation and earthmat laying at baneshwor substation work.



Figure 4.20: Site Visit by Technical consultant along with site technical team.

UPPER PILUWA KHOLA 3 HYDROELECTRIC PROJECT (4.95MW) SANKHUWASABHA, NEPAL UPDATED PROJECT SCHEDULE



Mon 4/17/23

1 of 1

MABILUNG ENERGY LIMITED

Upper Piluwa Khola-3 Hydroelectric Project (4.95MW) Sankhuwasabha, Nepal

List of Resources available

Contractor: Growth-PES J/V Date: 23 April, 2023

A. plant /machinery

S.No.	Particulars	Quantity	Remarks
1	Excavator	4 nos	
2	Backhoe Loader	1 nos	
3	Tripper	2 nos	
4	Tractor	1 nos	
5	Bolero pick-up	1 nos	
6	Crusher Plant	1 set	
7	Concrete pump	1 nos	
8	Concrete Mixture	3 nos	
9	Diesel Generator 40 kva	1 nos	
10	Hydraulic bar -Cutting machine	1 nos	
11	Dewatering pump 4 inch	4 nos	
12	Dewatering pump3 inch	4 nos	
13	Compression Testing Machine (2000kN)	1set	
14	Plate vibrator for cube test	1 set	
15	Slum test apparatus	1set	
16	Cube Mould	12 nos	
17	Copmaction testing apparatus	1 set	
18	Concrete vibrators	5 set	
19	Compaction Roller 2 ton	1 nos	

Contractor: Precise Hydro Engineering and construction Pvt. Ltd.

1	Diesel Generator 62.5 kva	1 nos	H/M contractor
2	Hydra 15-ton capacity	1 nos	H/M contractor
3	Welding machine	5 nos	H/M contractor
4	Tractor	1 nos	H/M contractor
5	Chain Pully	3 nos	

B.Manpower

1. Client Team

S.No.	Designation	Number	Remarks
1	Project Manager (Civil Engineer)	1	
2	Assistant Project Manager	1	
3	HM Incharge(Mechanical Overseer)		
4	Sub-Engineer	1	
5	Social Mobilizer	1	
6	Mechanical Incharge(Overseer)	1	
	Total	5	

MABILUNG ENERGY LIMITED

Upper Piluwa Khola-3 Hydroelectric Project (4.95MW) Sankhuwasabha, Nepal

List of Resources available

Contractor: Growth-PES J/V Date: 23 April, 2023

A. plant /machinery

S.No.	Particulars	Quantity	Remarks		
2. Civil contractor team (Growth /Pes JV)					

S.No.	Designation	Number	Remarks
5	Residental Engineer (Civil)	1	
6	Civil Engineer	1	
7	Civil Overseer	2	
8	Site Accountant	1	
9	Procument assistant	1	
10	Store keeper	1	
11	Electrician	1	
12	Mechanic	2	
13	Crusher operator	1	
14	Excavator overator	3	
15	Back- hoe operator	1	
16	Tripper driver	3	
17	Tractor driver	1	
18	Site Supervisor	4	
19	Bolero driver	1	
20	Cook	3	
21	Skilled labour	15	
22	Unskilled labour	20	
	Total	62	

3. Hydromechanical contractor (Precise Hydro Engineering) Team

		_	
S.No.	Designation	Number	Remarks
1	Mechanical Engineer	1	Site Incharge
2	Mechanical Supervisor	1	
3	Fitters	4	
4	Hydra operator	1	
5	Tractor driver	1	
6	Welder	6	
7	Helper	6	
	Total	20	
